



Calhoun: The NPS Institutional Archive
DSpace Repository

Reports and Technical Reports

Faculty and Researchers' Publications

2006

Total ownership cost reduction case study:
AEGIS microwave power tubes

Apte, Aruna U.; Dutkowski, Eugene

Monterey, California. Naval Postgraduate School

<https://hdl.handle.net/10945/586>

Downloaded from NPS Archive: Calhoun



Calhoun is the Naval Postgraduate School's public access digital repository for research materials and institutional publications created by the NPS community. Calhoun is named for Professor of Mathematics Guy K. Calhoun, NPS's first appointed -- and published -- scholarly author.

Dudley Knox Library / Naval Postgraduate School
411 Dyer Road / 1 University Circle
Monterey, California USA 93943

<http://www.nps.edu/library>



NAVAL
POSTGRADUATE
SCHOOL

MONTEREY, CALIFORNIA

Total Ownership Cost Reduction Case Study:

AEGIS Microwave Power Tubes

31 May 2006

by

Dr. Aruna U. Apte, Assistant Professor
Graduate School of Business & Public Policy, NPS

Eugene (Joe) Dutkowski
Naval Surface Warfare Center, Crane, Indiana

THIS PAGE INTENTIONALLY LEFT BLANK

**Naval Postgraduate School
Monterey, California**

RDML Richard H. Wells
President

Richard S. Elster
Provost

The Acquisition Chair, Graduate School of Business & Public Policy, Naval Postgraduate School supported the funding of the research presented herein. Reproduction of all or part of this report is authorized.

The report was prepared by:

Aruna U. Apte, Assistant Professor
Graduate School of Business & Public Policy

Eugene (Joe) Dutkowski
Naval Surface Warfare Center, Crane, Indiana

Reviewed by:

Robert N. Beck
Dean, Graduate School of Business & Public Policy

Released by:

Leonard A. Ferrari, Ph.D.
Associate Provost and Dean of Research

THIS PAGE INTENTIONALLY LEFT BLANK

REPORT DOCUMENTATION PAGEForm approved
OMB No 0704-0188

Public reporting burden for this collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington, VA 22202-4302, and to the Office of Management and Budget, Paperwork Reduction Project (0704-0188), Washington, DC 20503.

1. AGENCY USE ONLY (Leave blank)**2. REPORT DATE**
30 December 2005**3. REPORT TYPE AND DATES COVERED**
1 October 2004 – 30 September 2005**4. TITLE AND SUBTITLE**Total Ownership Cost Reduction Case Study:
AEGIS Microwave Power Tubes**5. FUNDING****6. AUTHOR (S)**Dr. Aruna U. Apte, Assistant Professor, Graduate School of Business & Public Policy
Eugene Dutkowski, Naval Surface Warfare Center, Crane, Indiana**7. PERFORMING ORGANIZATION NAME (S) AND ADDRESS (ES)**NAVAL POSTGRADUATE SCHOOL
GRADUATE SCHOOL OF BUSINESS AND PUBLIC POLICY
555 DYER ROAD
MONTEREY, CA 93943-5103**8. PERFORMING ORGANIZATION
REPORT NUMBER**
NPS-GSBPP-06-010**9. SPONSORING/MONITORING AGENCY NAME (S) AND ADDRESS (ES)****10. SPONSORING/MONITORING
AGENCY REPORT NUMBER****11. SUPPLEMENTARY NOTES****12a. DISTRIBUTION/AVAILABILITY STATEMENT**

Approved for public release; distribution unlimited

12b. DISTRIBUTION CODE**13. ABSTRACT (Maximum 200 words.)**

The goal of this research is to provide a descriptive case study that will chronicle the operational and engineering processes that were used to reduce the total ownership cost for the AEGIS Shipbuilding Project while dramatically improving the mean time before failure. The processes used to achieve these results are important to understand in light of current reduction in various resources in different programs. In particular, this case highlights the role that Naval Warfare Centers can and do play in the acquisition process.

14. SUBJECT TERMS

AEGIS, Total Ownership Cos, TOC, Mean time between failure, MTBF, Microwave Tubes, MWT, business processes, Cross Field Amplifier, CFA

**15. NUMBER OF
PAGES**
31**16. PRICE CODE****17. SECURITY CLASSIFICATION OF
REPORT: UNCLASSIFIED****18. SECURITY CLASSIFICATION OF
THIS PAGE: UNCLASSIFIED****19. SECURITY CLASSIFICATION OF
ABSTRACT: UNCLASSIFIED****20. LIMITATION OF
ABSTRACT:
UNLIMITED**

THIS PAGE INTENTIONALLY LEFT BLANK

Abstract

This research provides a descriptive case study that chronicles the operational and engineering processes that were used to reduce total ownership cost for microwave power tube components of the AEGIS Shipbuilding Project while dramatically improving their mean time between failure. The processes used to achieve these results are important to understand in light of the current reductions in various acquisition support resources including financial support, manpower and in-house technical expertise. In particular, this case highlights the role that Naval Warfare Centers can and do play in the acquisition process and its supporting engineering disciplines.

Keywords: AEGIS, Total Ownership Cos, TOC, Mean time between failure, MTBF, Microwave Tubes, MWT, business processes, Cross Field Amplifier, CFA

THIS PAGE INTENTIONALLY LEFT BLANK

Acknowledgements

We are grateful to RADM Jim Greene and Dr. Keith Snider for providing us this opportunity. Without Jim Greene's invaluable insights, this project would not have been possible. We would also like to thank Keith for his expert comments on the substance of the research. Additional thanks go to Karey Shaffer for her constant support throughout the duration of this project.

THIS PAGE INTENTIONALLY LEFT BLANK

About the Authors

Dr. Aruna Apte is an Assistant Professor in the department of Logistics, Graduate School of Business and Public Policy, at the Naval Postgraduate School, Monterey, California. She received her PhD in Operations Research from the School of Engineering at Southern Methodist University in Dallas, Texas. Her earlier education includes a Master's in Mathematics and credits toward a PhD in Mathematics from Temple University, Philadelphia, Pennsylvania. She has taught in the Cox School of Business, School of Engineering and the Department of Mathematics at Southern Methodist University. She has over twenty years of experience in teaching operations management, operations research, and mathematics courses at the undergraduate and graduate levels in the resident and distance learning programs.

Apte has successfully completed various research projects involving applications of mathematical models and optimization techniques. Her research interests are in the areas of developing mathematical models and algorithms for complex, real-world operational problems using techniques of combinatorial optimization, network programming, and mixed-integer programming based on heuristic search methods. She is interested in developing theoretical concepts in mathematical programming. It is also important to her that her research is directly applicable to practical problems and has significant value-adding potential. Her research articles have been published in prestigious journals including *Naval Research Logistics* and *Interfaces*. She has published one article, and two are forthcoming, in the *Acquisition Research Sponsored Report Series, GSBPP, NPS*. She also has a patent pending for "SONET Ring Designer Tool," created when she worked as a consultant for MCI.

Mr. Eugene (Joe) Dutkowski is the Vacuum-Electron Device Branch manager at the Naval Surface Warfare Center Crane, Crane Indiana. He received his Master's of Electrical Engineering degree in 1976 from the University of Louisville in Louisville, Kentucky specializing in Antenna theory. Undergraduate degree in

Electrical Engineering from University of Louisville was received in 1975. Mr. Dutkowski has worked in the field of Vacuum electronics for 30 years developing microwave sources for DoD weapons systems. Currently, Mr. Dutkowski supports the Naval Sea Systems Command (NAVSEA) as functioning DoD Executive Agent for Microwave tubes and as the In-Service Engineering agent for all the Navy's surface radar tubes.

Table of Contents

Introduction	1
Background.....	1
Greene's Story	2
The MWT	3
The Problem	7
The Opportunity	8
Greene's Solution	8
The Process.....	10
The Accomplishment	12
The Analysis	15
Business Issues	17
Conclusion	21
List of References	22
Initial Distribution List	24

THIS PAGE INTENTIONALLY LEFT BLANK

Introduction


All ships of the AEGIS fleet, indeed the entire fleet, require Microwave Tubes (MWT) (Hoffer, 2003). Early in the development of the AEGIS program, one such MWT, the Cross Field Amplifier (CFA) proved to be a substantial cost driver. This study documents the identification of the root causes of this problem and the process that not only eliminated the problem but also yielded both an increase in tube mean time between failure (MTBF) and a much-lowered total ownership cost (TOC). This case chronicles the methods used to reduce TOC in a program that serves as an example of early spiral development. The objective of this study is to understand the process and recognize the business issues within it that are essential to maintaining system combat capability, enhancing system affordability and reducing TOC.

Background

The AEGIS shipbuilding program, arguably one of the largest and most successful acquisition programs in the Department of Defense (DoD), has provided the Navy with over 90 capable surface combatant ships. AEGIS ships now make up the majority of the Navy's destroyer and all of its cruiser fleet. MWTs are used in 27 CGs and 48 DDGs to date (Hoffer, 2003) and this number continues to grow. MWTs are the primary components in the radar systems of the AEGIS fleet. There are numerous other shipboard systems that utilize MWTs: SPS-48, SPS-49, MK-99, USC-38, and Phalanx to name just a few. Throughout the world, 57% of MWTs are used in radars; the manufacture of radar MWTs alone is a \$280.3M market. Figure 1 shows the world market for MWTs by application and type (Dutkowski, 2004-2005).

Figure 1. The World Market for MWTs by Application and Type

Source: Dutkowski, E.J., Jr. (2004-2005)

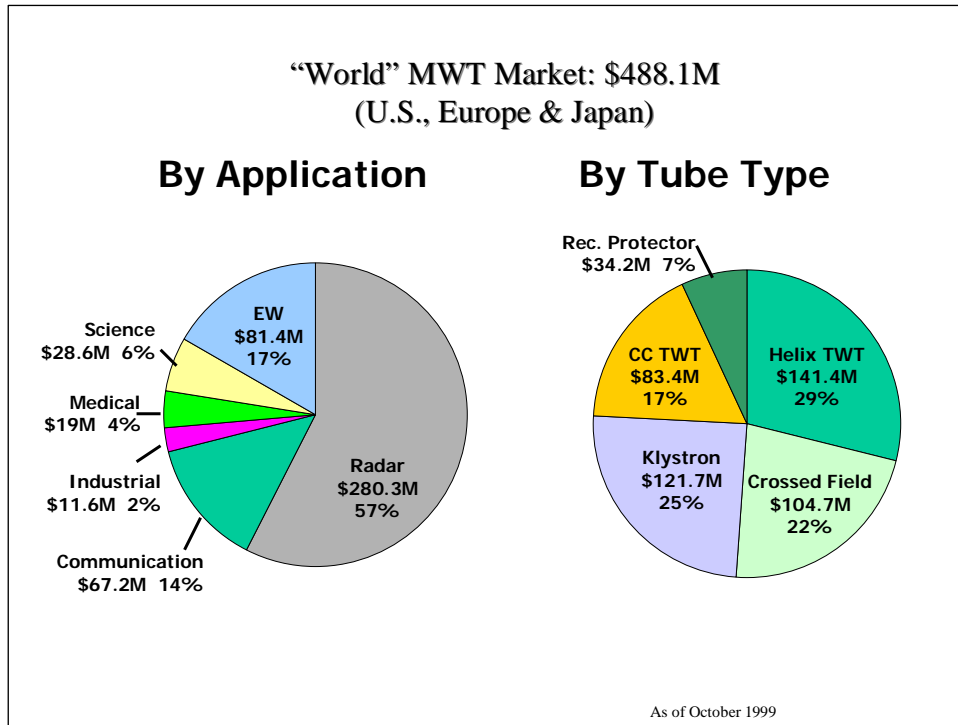


Greene's Story

It was the early 1980's, the height of the Reagan defense build-up, and AEGIS was the centerpiece of the Navy's shipbuilding program. Rear Admiral James B. Greene, Jr. was the project manager (PM) for the AEGIS shipbuilding project. Initial deployment of AEGIS cruisers was completed and departmental focus was shifting to include lifecycle cost control as well as enhanced system operational availability (Ao). At the same time, the DDG-51 class was in engineering design and development. The weapons systems of the ships were heavily dependent on MWTs with Cruisers using 176 per system and Destroyers 90. Figure 2 provides a picture of the MWTs used on these ships. Not surprisingly, MWTs became cost drivers for TOC and also for system, and thus ship, Ao.

Figure 2. Tubes used in the AEGIS Weapons System

Source: Dutkowski, E.J., Jr. (2004-2005)

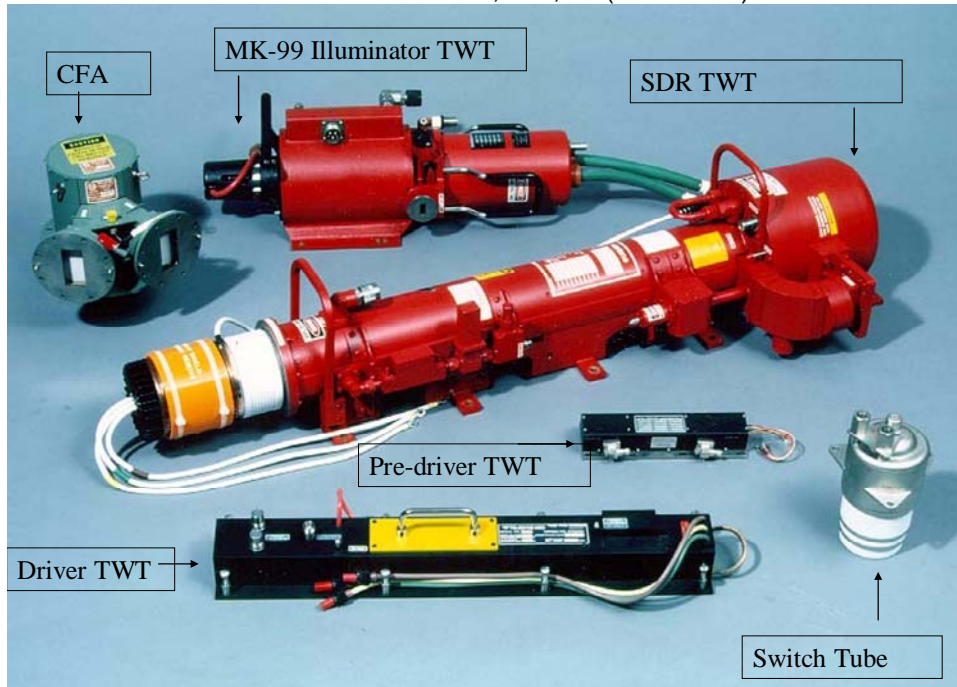

In a regular monthly meeting with his staff, Admiral Greene was briefed on the status of MWTs. These meetings were held to review program execution, cost and schedule issues. Staff noted that the unit cost of MWTs had exceeded their expectations and that the mean time between failure (MTBF) of MWTs was very low. This situation had existed for some time with no improvement in sight without added management attention.


The MWT

The AEGIS weapons system had been in design and development for several years. Program decisions were based on, among other considerations, reliability estimates that included MWT reliability, cost estimates, and maintenance concepts. The use of MWTs in combat systems was extensive. The principals in the program—designers, planners, and decision-makers including contractors—knew the extent of the applications of MWTs in AEGIS ships. There was not just one type of MWT; several different MWTs were utilized in AEGIS ships, for instance, Cross Field Amplifiers (CFAs) in the radar systems and traveling wave tubes (TWTs) in

electronic warfare systems. Though there were numerous applications of MWTs then, now they are used in even more war-fighting applications. Figure 3 (Dutkowski, 2004-2005) shows a current example of MWT utilization in a CG-47 class ship.

Figure 3. CG-47 Class MWT-based Systems

Source: Dutkowski, E.J., Jr. (2004-2005)

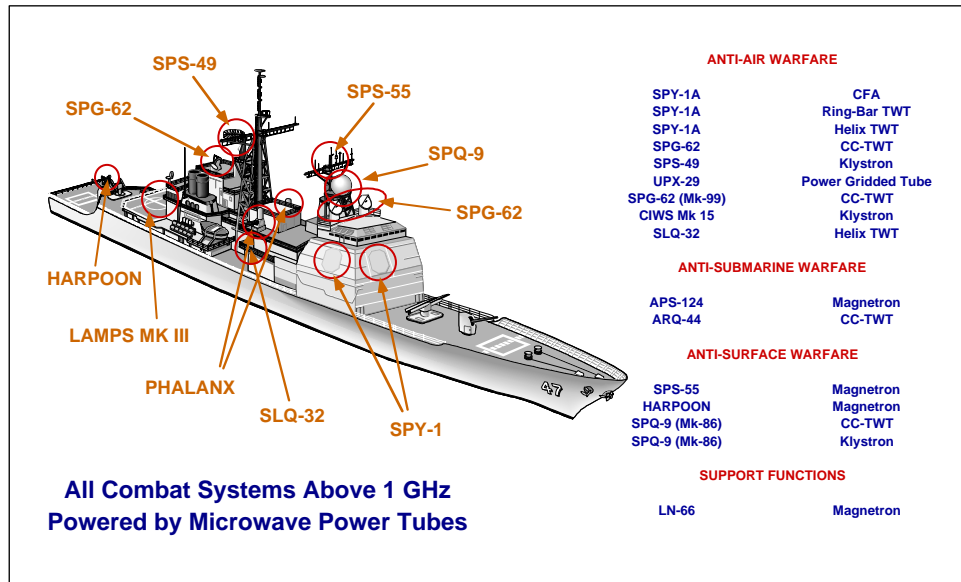

As can be seen, many shipboard systems depend on MWTs. Figure 4 (Dutkowski, 2004-2005) illustrates the usage of MWTs in various such systems. The prevalence of MWTs in Navy ships is shown in Figure 5.

Figure 4. Usage of MWTs
 Source: Dutkowski, E.J., Jr. (2004-2005)


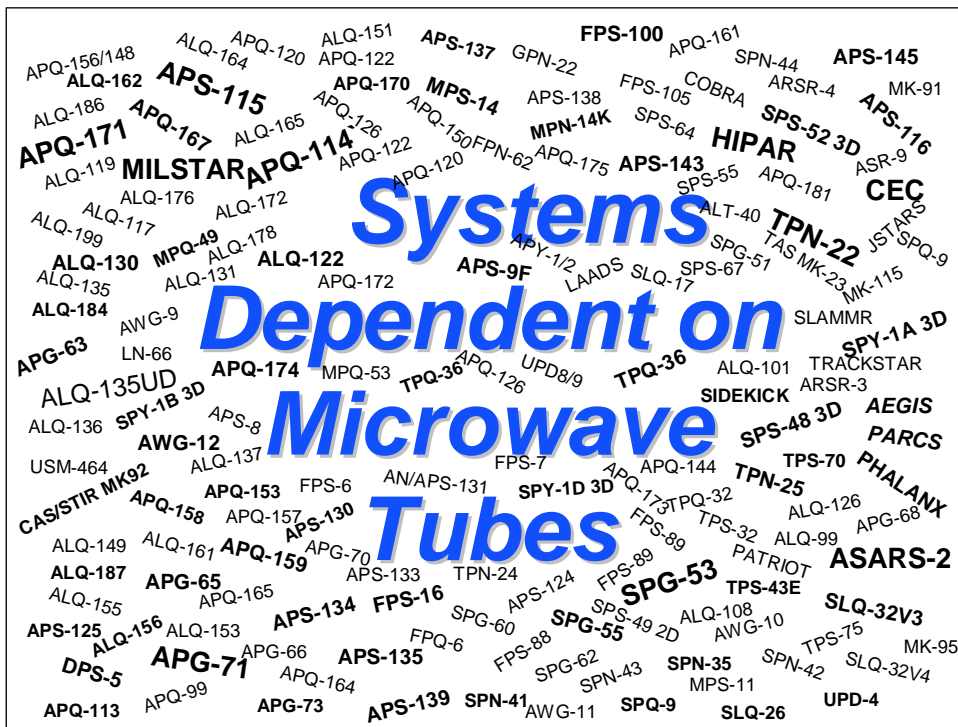


Figure 5. Current MWT Usage in the US Navy
 Source: Dutkowski, E.J., Jr. (2004-2005)

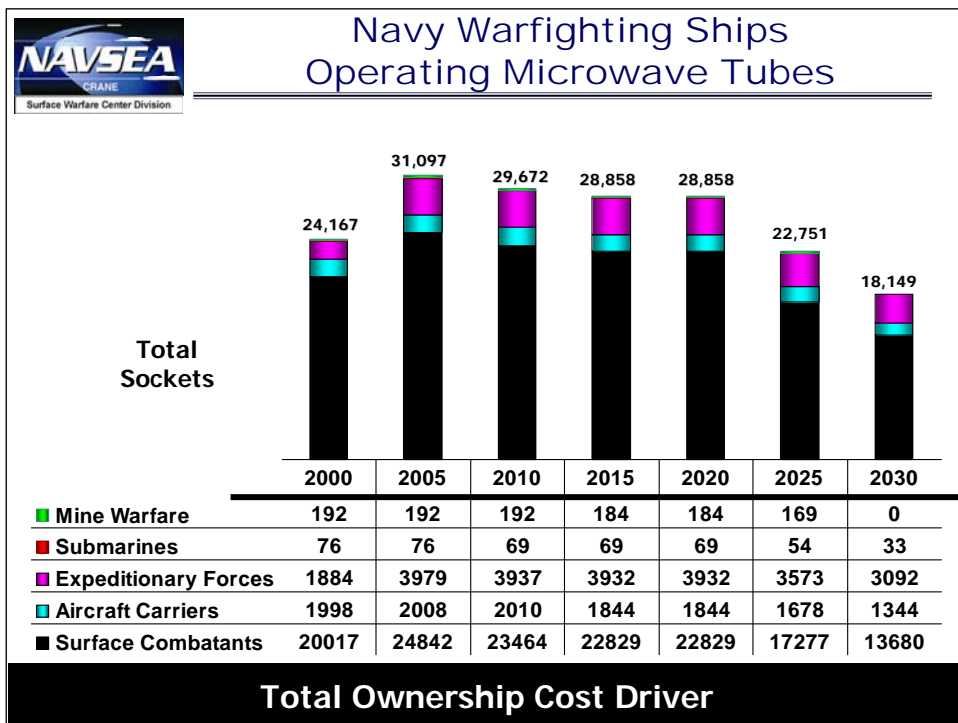

When RADM Greene was briefed by his staff, the manufacture of MWTs was an industry that was very process and material dependent with little process or configuration control. The tubes were, indeed, state-of-the-art technology for that era but they were, in the current vernacular, early “spirals” (Apte 2005). Each succeeding version was an evolved version of the previous one. This situation presented great challenges to the team to put controls in place in the manufacturing plants to reduce manufacturing risk. Through contract requirements (requiring configuration and process controls), investment of government dollars into product improvements and continual monitoring of product, these factors could be mitigated over time.

Given the unit cost and MTBF data of the MWTs, the PM estimated tube replacement costs to be \$1M/ship/year. Based on a then projected AEGIS fleet size of 40 ships, Admiral Greene calculated total annual cost for CFA tube replacement to be \$40M—just to keep the AEGIS radar systems operational.


The Problem

The data presented to Admiral Greene highlighted that MWTs were costly to replace and costly to produce. With MTBF in the range of 1,300-12,000 hours and a high unit cost, they were a major contributor to TOC.

The key players in the program understood the risks involved in the "black art" of MWT production. This set the stage for tasking Warfare Center engineering specialists to take charge of this issue and craft engineering and logistics solutions. In any case, performance-versus-cost of MWTs was a problem and not using the tubes was not a technical solution.

A parallel and nagging question of the day was that if MWTs are so difficult and expensive to produce (and at the same time essential to so many applications of AEGIS), then why not replace the tubes with solid-state components? This issue took considerable engineering expertise and time to answer with Figure 6 being developed to silence the critics. Simply put, the solid-state technology at that time was not mature enough to replace the vacuum devices.

Figure 6. Microwave Components Military Essential Electronics
 Source: Dutkowski, E.J., Jr. (2004-2005)

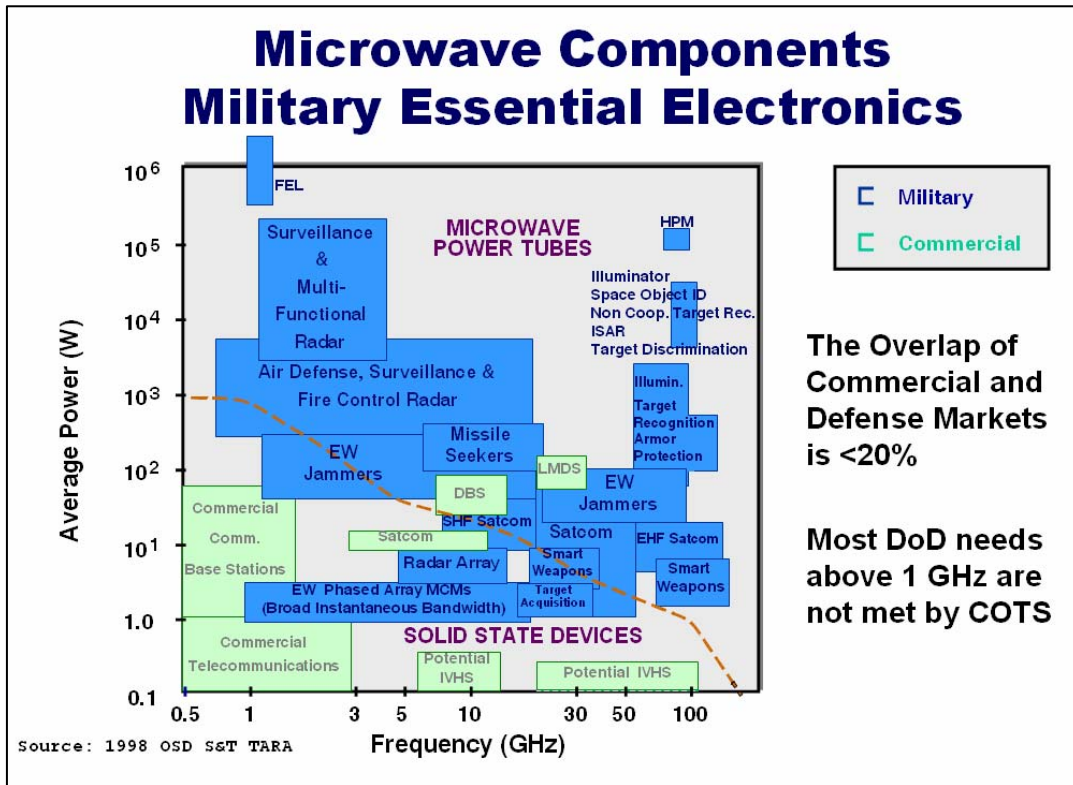

The Opportunity


Admiral Greene was facing quite a few issues revolving around the MWT components. But an opportunity presented itself. There was soon to be a conference held at the Naval Postgraduate School (NPS) on MWTs. The CEOs of all the companies that provided MWTs to the AEGIS shipbuilding project were attending the conference. The companies would both benefit from the success of AEGIS and would suffer if the performance/cost of MWTs remained the same. Admiral Greene sensed the potential for turnaround.

Greene's Solution

Admiral Greene decided that instead of treating adversity as a constraint, he was going to exploit the same to solve the problem. He made a pitch specifically to the CEOs of the vendor companies. Focusing on CFAs, he explained to them that the problem he was facing was that CFAs had an operating cost of \$1M/ship/year.

He conveyed to them the criticality of CFAs to the AEGIS fleet. Figure 7 depicts the CFA and its prevalence in the AEGIS fleet. At the microwave power tube conference he challenged them, "Propose something to fix this problem. Let us work together. As Project Manager, I promise you full cooperation. Let us collaborate and resolve this issue." At Admiral Greene's invitation, the CEOs came to his quarters in Hermann Hall at NPS. A frank dialogue at this meeting laid the groundwork for implementing a successful process that ultimately led to a reduction in TOC and an increase in MTBF for CFAs. Although limited contractually on the extent he could be involved in internal company affairs, Admiral Greene did offer all the CEOs the opportunity to have him speak to each of their work forces to underscore the importance of their efforts in this critical national defense program.

Figure 7. AN/SPY- 1 CFA
 Source: Dutkowski, E.J., Jr. (2004-2005)

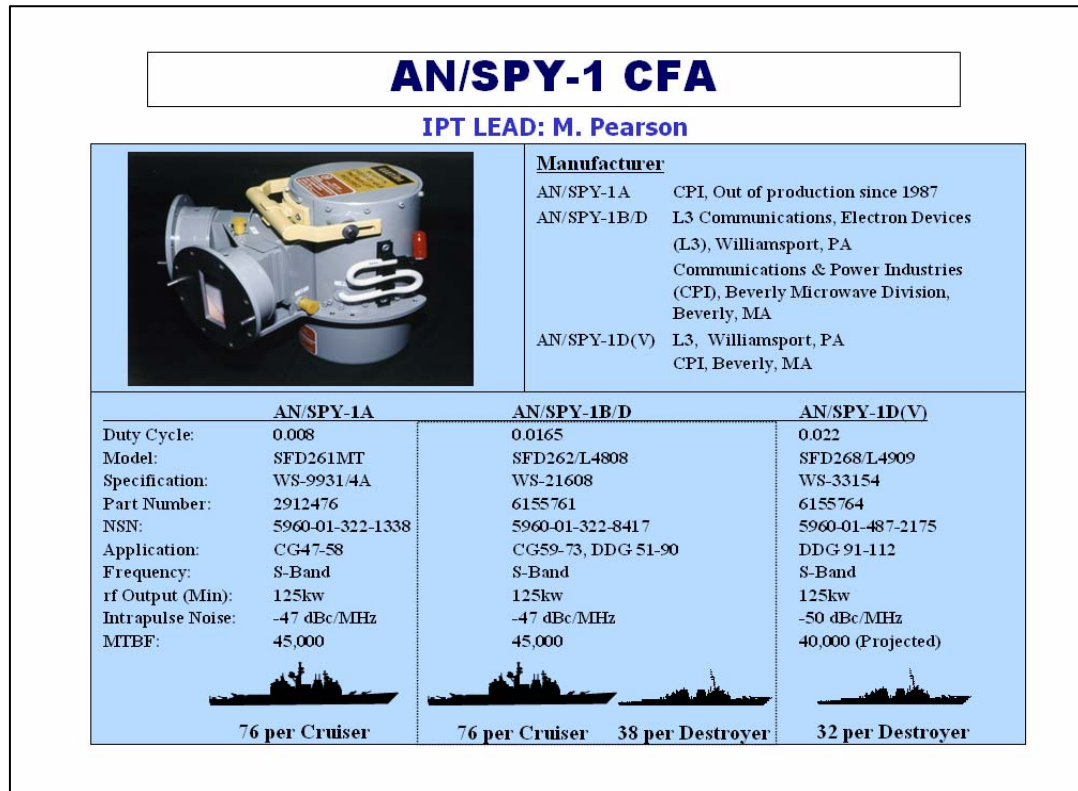

The Process

As he had agreed, Admiral Greene visited each of the tube production facilities with his staff. This staff included staff engineers, operations managers, and financial experts from the Naval Surface Warfare Center at Crane Indiana, the Navy's In Service Engineering Agent (ISEA) for microwave power tubes. He challenged his staff to devise a solution. He felt confident they could do so because of the technical competence they demonstrated through the years in combat systems engineering and in particular microwave power tube technology.

After initial evaluation, staff proposed a two-fold approach to the combined TOC/MTBF issues. The first was to assure an accurate diagnosis and repair of the tube (Hoffer, 2003); the second was an improved ability to locate and track all tubes that had been produced (Dutkowski, 2004-2005). Initial diagnostic trouble shooting

revealed a metallurgical problem. The anode of the CFA was made of high purity, electrical-grade copper which is quite soft. This copper also has a very low melting point. When a CFA turns on or during the change to a long waveform, the CFA has a tendency to arc between cathode and anode. Excessive arcing leads to premature failure and is detrimental to the overall performance of the amplifier. Admiral Greene's team discovered that the anode vanes were melting slightly and progressively due to arcing. The deterioration due to arcing was increasing—to the point that the tube would arc at shorter pulse lengths and at lower power levels. This erosion eventually led to tube failure. It was clear that better operating life could be obtained if the anode vanes could be prevented from melting due to arcing. The solution devised was to add a thin layer of molybdenum, which has a higher melting point than copper, at the ends of the anode vanes and to reduce the arcing by better processing of the tubes.

The second issue to be resolved was an inventory control issue. The CFAs were high value assets and capturing them for repair vice disposal was crucial. This required knowing where each tube was and then providing for their return to the designated repair facility. Additionally, tubes with the new modifications needed to be installed where and when appropriate so they could fit the empty sockets left by the un-improved tubes. Therefore, tracking the CFAs was vital. The team developed a method of serial number tracking of each tube. The principal behind it was the same as that behind the now common barcode and the recently introduced technology of radio frequency identification (RFID). The Crane team successfully implemented a serial number tracking program. The Crane team was successful for two reasons: they had in-house technical skills to successfully develop engineering solutions to the arcing problem and they had the managerial skills necessary to develop an effective inventory control and repair protocol. This process, in addition to configuration control of the manufacturing, added the ability to track changes introduced through the spiral development process to give visibility to the impact these changes had on performance.

At the next biennial conference, Admiral Greene presented the results to industry as a "good improvement." Thanks to the improved tracking and repair processes of CFAs, the MTBF had increased substantially—to about 5000 hours (Greene, 2004)—and the operating cost was reduced by a third. However, he challenged his staff and industry to keep building on the three pillars for success of the initiative: accurate tracking of tubes, maintenance of the knowledge base necessary to stay abreast of technical developments in the tube industry and continuous improvement of the tube production process.

After his departure from the program, these initiatives continued to thrive at Crane Naval Surface Warfare Center. It is still operating with increasingly impressive statistics: MTBF is up to 40,000-45,000 hours, and the cost per operating hour in 2002 dollars has been reduced to \$0.45/socket from \$8.20/socket as shown in Figure 8 (Dutkowski, 2004-2005).

The Accomplishment


The success of initiatives such as inventory control using accurate tracking, maintaining technical knowledge base, and continuous improvement of the production process, has tremendous significance to the support of any combat system. The solution implemented regarding the CFA components in AEGIS is an excellent example of a successful pursuit of reduction of TOC (Boudreau & Naegle, 2003). The effort initiated in the mid-1980s is still paying off. The arcing that led to the melting of anodes (which, as mentioned above, precipitated the failure of CFAs—resulting in a very low MTBF) prompted a series of well-managed steps to continue to improve the tubes. Tracking of the tubes was essential for locating and tracking the result of the changes. This was an extremely valuable initiative since it helped reduce the cycle-time for repair and change insertion by the real-time feedback to the manufacturer. Knowing what caused the failure and where and when the failure occurred was critical to increasing operational availability. The ability to track the CFAs was critical to the success of the program. Likewise, an impressive string of engineering changes such as the modification in anode metallurgy, manufacturing processes improvements, controls, logistics, and

configuration control have led to an increase in the MTBF of the tubes from 6000 hours to 40,000-45,000 hours.

These improvements have reduced the frequency of corrective maintenance and, therefore, the operating and support (O & S) costs. The changes in vane tips, tracking of MWTs (so that the location and circumstances of MWT malfunctions are known), and extra attention to business issues have dramatically improved the reliability and availability of the host weapons system. Of note, this same modification of the vane tips has been implemented in two other CFA configurations thus using the learning to advance the design of new systems. Other AEGIS MWTs have also undergone additional improvements and have yielded added O & S cost savings. Progress in reducing the cost/operating hour of AEGIS CFA tubes is shown in Figure 8 (Dutkowski, 2004-2005).


Figure 8. Cost/Operating Hour History

Source: Dutkowski, E.J., Jr. (2004-2005)

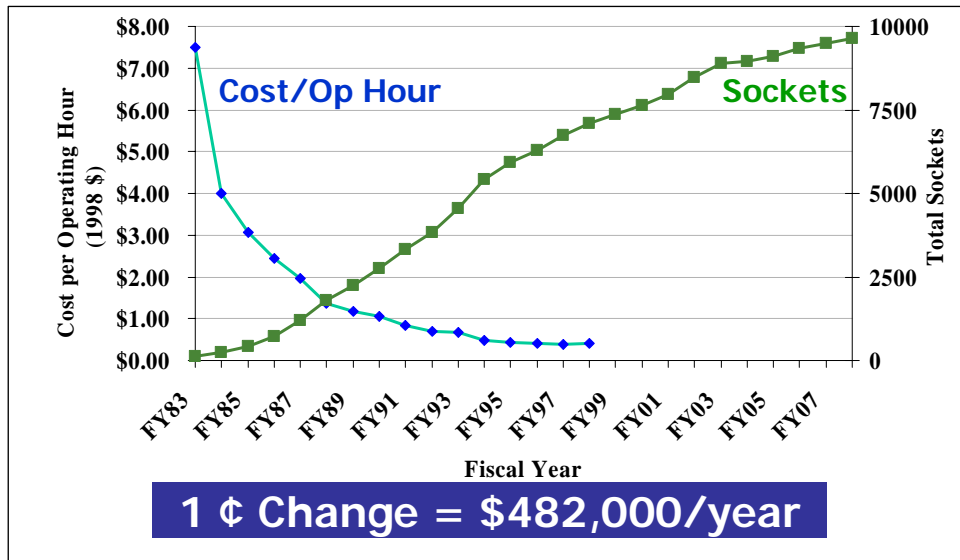

Even if just a small amount is saved on each tube, due to the large number of tubes used in the fleet, savings can be substantial for a small change in life-cycle cost. The V-chart in Figure 9 shows that investment in engineering and management initiatives throughout the lifecycle of a system can dramatically reduce TOC. This initiative has found application in 27 AEGIS cruisers (each of which includes 76 CFAs) and 48 AEGIS destroyers (each equipped with 32 to 38 CFAs) to date. In 2002 dollars, the annual savings averaged about \$1.9 million per AEGIS cruiser and \$950 thousand per AEGIS destroyer.

Figure 9. AWS Microwave Tube Engineering/Acquisition Program
 Source: Dutkowski, E.J., Jr. (2004-2005)

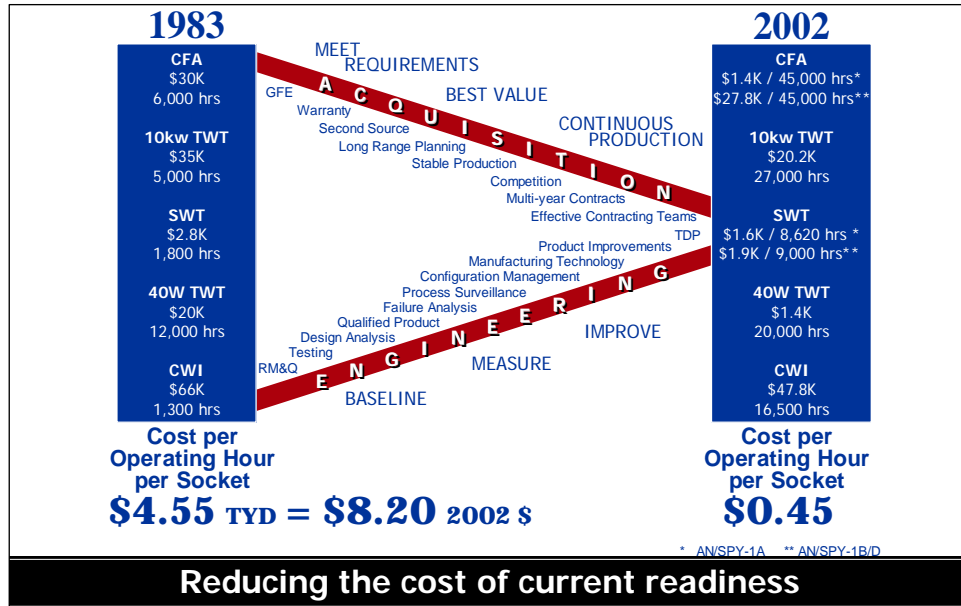

The Analysis

Several key factors contributed to the success of this initiative. The program achieved a high level of collaboration amongst all key parties including the Fleet, field activities and headquarters. In order for a project to succeed across functional departments such as design, planning, contracting and engineering, there needs to be a leader who will champion the new initiatives and processes. This leader, along with key team players, has to devise innovative programmatic and contractual provisions. Greene's ability to integrate his team was a key element in that team's success and he was able to leverage the existing AEGIS team to do so. The concept of an Integrated Product Team (IPT) is an initiative common today, but was not a by-word 20 years ago. Likewise, although theoretically the use of an IPT is an effective business tactic, the difficulty in its implementation can be overcome only if a clear focus and vision is maintained by the team leader.

In addition to the strength of Greene's leadership, none of these successful steps could have been achieved without the in-house (government) technical

competence and knowledge of Greene's staff. In-house technical knowledge was essential to assuring industry collaboration. A knowledgeable (smart) buyer is essential in evaluating industry recommendations for technical and process changes. Consequently, retaining in-house expert technical personnel is critical to improving system operations and costs. These assets may be in the field or at headquarters or both, but they must exist on the government team.

The above discussion of the small industrial base and process/material dependent manufacturing of the CFA suggests that there are very few, sometimes no, manufacturers for customized defense products. Due to this lack of competition, integrity has to be maintained in writing the best value contracts. It has been proven in the private sector over and over again that competition breeds both diversity in products and helps the best among them to survive. The absence of competition in the manufacturing of some defense products adds responsibility to the program manager; he/she must ensure the quality of the product and contract. Therefore, evaluating best value contracts is key in this type of acquisition. Many times the government must buy critical product in a small production lot environment, precluding the ability to have a competitive contract situation. The small production lot environment requires competent government oversight to be effective. Again, one must have technically competent staff within the government to do so.

In addition, the production pipeline of such customized defense products has to be smooth to achieve significant cost savings. A disruptive supply will likely stifle MTBF improvements. The stop-and-start of production adds the disadvantage of a high fixed cost. Therefore continuous production is desirable. This requires a procuring agency that views long-term requirements and vendor loading versus the short-term (meet the current demand) perspective. This continuity is especially necessary when manufacturers are training workers for such tailored products. In the case of the CFA, the very stable AEGIS shipbuilding project provided just such a stable demand for CFAs

Business Issues

On the surface, this discussion is a simple success story of identifying CFA failures due to arcing and engineering their prevention by tracking and modifying the tubes, thereby increasing MTBF, and at the same time lowering production costs. What is impressive and powerful about this accomplishment is the process through which the problem was diagnosed and the cure implemented. “In my wildest dreams, I did not think we could come this far,” said Greene about the success of this program (Greene, 2004). What is crucial to this discussion is the recognition that this process has long-reaching roots in Acquisition strategy—then and now. This detection, analysis, and solution process encompasses profound technical, managerial, and policy issues. Some of the business issues this story highlights—such as organizational integration, evolutionary acquisition, theory of constraints, the six sigma/ continuous improvement theories of total quality management, outsourcing, operations management, and contract/cost/budgets, are instructive for any program manager.

The dramatic improvement implemented by Greene and his team was and is a result of organizational integration of key players, an IPT in today’s vernacular. This collaboration included the AEGIS Program Office, Communications and Power Industries (CPI, a vendor that was formerly part of Varian and provided the CFA), Crane Naval Surface Warfare Center, the Navy Man Tech Office, and *Raytheon* (the prime contractor). The collaborative effort for reduction in TOC and increase in MTBF of the CFA had two major facets: acquisition and engineering. Individuals from these disciplines formed the integrated product team.

The evolving production of the CFA reminds the researcher of the current strategy of Evolutionary Acquisition and its process of Spiral Development (Apte, 2005). There are similarities between the process through which the CFAs evolved and the current trends of incremental design and production based on the input of warfighters. Spiral Development is a set of acquisition activities that are incorporated in an evolving baseline using increments. Each increment increases the capability of the product. Each increment is completed at a rapid pace. Each increment builds

over each previous spiral. Since all the CFAs were customized products, each version that was produced was a modification of the previous version. The versions were redesigned based on user input so that the lessons learned from the previous version helped reduce the flaws in the production of the next version. Each increment included a reassessment of risks and assumptions. These are also the basis of Spiral Development. These days each increment creates a functioning prototype at the end of which lessons learned are evaluated; before starting the next increment, a decision is made about whether to proceed or not. In essence, the CFA evolution is an early example of what is now termed spiral development.

Numerous program challenges existed in the form of resources, constraints, new and evolving technologies, lack of understanding of failure root causes, and communications between program participants across the country to name a few. But, the theory of constraints suggests that such constraints can be exploited to the advantage of the system. In the presence of constraints, one need first identify the system constraints. Next, one should decide how to exploit them. Thirdly, one should subordinate everything else to this decision. Lastly, one should remove the system constraints to solve the problem. That is precisely what was done here. For example, Greene exploited the high unit production cost and low MTBF by challenging the manufacturers to discover a process which would deliver a quality tube to the program, increase MTBF and reduce TOC.

One of the important tools in Total Quality Management is the Cause-and-Effect diagram, sometimes known as the fish-bone or Ishikawa diagram. This diagram is used to sort out the causes of the problem. Brainstorming sessions of groups of personnel involved are required. These sessions help identify complete lists of causes of the problem and the relationship between causes and effects in a rational manner. This process educates everyone involved in the system regarding the causes and effects of the problem. This engineering process revealed the melting of the CFAs during arcing. By asking questions such as: Why did the tube fail? Why did the vanes melt? What was the cause of low melting point? Why cannot

the solid state be used? Greene's team was able to expose and correct the root cause of the low MTBF statistics for the CFAs.

The literature and current research in outsourcing indicates that outsourcing products, not service, is more advantageous to most systems, especially where the service involves the defense of a nation. Outsourcing the support of a weapon system eliminates the need for in-house technical knowledge. Absence of such personnel prohibits creative approaches to system failures. It also inhibits challenges to the industry that supports the same system. Decreasing or eliminating the retention of in-house experts in certain services may prove to be penny wise and pound foolish.

As noted earlier, the evolution of the AEGIS CFAs presents an early example of what is now termed spiral development. As such, since spiral development is the preferred acquisition strategy in DoD today, this CFA case has even more relevance. If new weapons systems in DoD are going to be largely spiral in nature, then there will be many future opportunities to replicate the CFA evolution. If TOC of weapons systems are to be constrained, then program officers must be prepared to emulate the CFA strategy described herein. This will require the maintenance of a technically competent work force both at program inception and during system deployment. This later role has been historically filled in the Navy by competent ISEAs resident in Naval Warfare Centers, which each specialize in particular technologies. The author suggests, using this CFA case as an example, that it is imperative that this skill set be maintained if DoD hopes to contain TOC in a spiral development world. Colvard and Doyle (2006) reach a similar conclusion albeit on a broader organizational scale.

The CFA case also raises the notion that it is crucial for a DoD entity to play a "stewardship" role when necessary to preserve DoD's ability to obtain an affordable product/process which is critical to national defense needs. Such a role is envisioned when products or processes have limited commercial interest and support, on-shore sources are non-existent or insufficient, and/or unique military

logistics requirements exist. In a stewardship role, a facility such as Crane Naval Surface Warfare Center would facilitate communication and knowledge sharing among industry, academia and military users of products and processes. The center would also maintain crucial capabilities and knowledge required for test and evaluation, Logistics, and for certain manufacturing and repair. This stewardship would also identify and assure support of technologies underlying the product or process. Last, but definitely not the least, there needs to be an entity that will serve as an advocate for programs targeted at maintaining the viability of the product or process and work to maintain a balanced budget strategy to support the critical industrial base. This notion makes yet another argument, proven in the CFA case, for retaining an in-house technically competent workforce and a Industrial Stewardship program.

One of the most important aspects of operations management is process management. Process management is an ongoing methodology for evaluating, analyzing, and improving the performance quality of a key business process. A process is evaluated by establishing process ownership, determining user requirements, and evaluating and rating the process. This process is then analyzed by benchmarking, developing and reviewing solutions with participants, and developing improvement plans. Process improvement is then achieved by implementing the process improvement plan, measuring the results, obtaining user feedback and, at the end, doing it all over again. Clearly, without such a continuous process improvement strategy, the CFA program would not have achieved such impressive results. Key to the success of this process is configuration control and the tracking of the product.

Conclusion

The goal of this research was to provide a descriptive case study that chronicled the operational and engineering processes used to reduce one aspect of the total ownership cost for the Aegis Shipbuilding Project. In the early days (circa 1983) of the Aegis Shipbuilding Project, the program office recognized that the numerous microwave tubes used in the Aegis radar system would significantly contribute to operational costs. As a result, an initiative was put in place to focus on substantially reducing these costs. The initiative was eventually applied across the whole spectrum of Navy microwave power tubes. This Reduction in Total Ownership Cost (R-TOC) effort has been extremely successful as various initiatives have driven down cost metrics (such as dollars/operating hour) while achieving a significant increase in MTBF. The engineering and management processes used to achieve these results are important to understand in light of recent manpower reductions in the services as well as an erosion of the in-house engineering skill base. In particular, this case highlights the role that Naval Surface Warfare Centers can and do play in the acquisition process. This case study validates these successes and identifies the underlying factors that catalyzed them.

THIS PAGE INTENTIONALLY LEFT BLANK

List of References

- Apte, A. (2005, June), Spiral Development: A Perspective, (Acquisition Research Sponsored Report Series), Monterey, CA: Naval Postgraduate School.
- Boudreau, M. W. & Naegle, B.R. (2003, September). Total ownership cost considerations in key performance parameters and beyond (Acquisition Research Sponsored Report Series). Monterey, CA: Naval Postgraduate School.
- Colvard, J.E. & Doyle, J.H. (2006, February). We Need Scientists--Engineers More than Ever, U.S. Naval Institute Proceedings.
- Dutkowski, E.J., Jr. (2004, September 2 through 2005, July 28). [Electronic Communication and phone interviews with Aruna Apte].
- Greene, J.B., Jr. (2004, September 28 through 2005, December 2). [Interviews and Electronic Communication with Aruna Apte].
- Hoffer, K. (2003, November 17). [Electronic Communication with Aruna Apte].

THIS PAGE INTENTIONALLY LEFT BLANK

2003 - 2006 Sponsored Acquisition Research Products

Acquisition Case Series

[NPS-AM-06-008](#) Apte, Aruna U. and Eugene Dutkowski. Total Ownership Cost Reduction Case Study: AEGIS Microwave Power Tubes. May 2006.

[UMD-CM-05-019](#) Lucyshyn, William, [Rene Rendon](#), and Stephanie Novello. Improving Readiness with a Public-Private Partnership: NAVAIR's Auxiliary Power Unit Total Logistics Support Program. July 2005.

[UMD-CM-05-018](#) Lucyshyn, William, and Stephanie Novello. The Naval Ordnance Station Louisville: A Case Study of Privatization-in-Place. August 2005.

[NPS-CM-04-008](#) Lucyshyn, William, [Jeffrey Cuskey](#), and Jonathan Roberts. Privatization of the Naval Air Warfare Center, Aircraft Division, Indianapolis. July 2004.

[NPS-PM-04-010](#) Lucyshyn, William, [Keith F. Snider](#), and Robert Maly. The Army Seeks a World Class Logistics Modernization Program. June 2004.

[NPS-CM-03-005](#) [David V. Lamm](#). Contract Closeout (A). September 2003.

Sponsored Report Series

[NPS-LM-06-005](#) Hernandez, Captain Emeterio V., US Air Force and Lieutenant Christopher A. Thomas, US Navy. Investigating the Department of Defense's Implementation of Passive Radio Frequency Identification (RFID). December 2005.

[NPS-FM-06-004](#) Rios, Jr., LCDR Cesar G., US Navy. Return on Investment Analysis of Information Warfare Systems. September 2005.

[NPS-AM-06-003](#) Komoroski, Christine L. Reducing Cycle Time and Increasing Value through the Application of Knowledge Value Added Methodology to the U.S. Navy Shipyard Planning Process. December 2005.

[UMD-AM-05-021](#) Gansler, Jacques S., and William Lucyshyn. A Strategy for Defense Acquisition Research. August 2005.

[UMD-CM-05-020](#) Dunn, Richard. Contractors in the 21st Century "Combat Zone." April 2005.

[NPS-PM-05-017](#) Brianas, Christopher G. Department of the Navy Procurement Metrics Evaluation. June 2005.

[NPS-CM-05-015](#) Johnson, Ellsworth K. III, Bryan H. Paton, Edward W. Threat, and Lisa A. Haptonstall. Joint Contingency Contracting. June 2005.

[NPS-CM-05-013](#) Schwartz, Brett M., Jadon Lincoln, Jose L. Sanchez, and Leslie S. Beltz. Update of the Navy Contract Writing Guide Phase III. June 2005.

[NPS-PM-05-012](#) Jenkins, Glenn E., and William J. Snodgrass, Jr. The Raven Small Unmanned Aerial Vehicle (SUAV): Investigating Potential Dichotomies between Doctrine and Practice. June 2005.

[NPS-FM-05-009](#) [Jones](#), Lawrence R., [Jerry McCaffery](#), and Kory L. Fierstine. Budgeting for National Defense Acquisition: Assessing System Linkage and the Impact of Transformation. June 2005.

[NPS-LM-05-008](#) [Kang](#), Keebom, [Kenneth Doerr](#), [Michael Boudreau](#), and Uday Apte. A Decision Support Model for Valuing Proposed Improvements in Component Reliability. June 2005.

[NPS-PM-05-007](#) [Dillard](#), John T., and [Mark E. Nissen](#). Determining the Best Loci of Knowledge, Responsibilities and Decision Rights in Major Acquisition Organizations. June 2005.

[NPS-AM-05-006](#) [San Miguel](#), Joseph G., [John K. Shank](#), and [Donald E. Summers](#). Navy Acquisition via Leasing: Policy, Politics, and Polemics with the Maritime Prepositioned Ships. April 2005.

[NPS-CM-05-003](#) [Rendon](#), Rene G. Commodity Sourcing Strategies: Supply Management in Action. January 2005.

[NPS-CM-04-019](#) Lord, Roger. Contractor Past Performance Information (PPI) In Source Selection: A comparison Study of Public and Private Sector. December 2004.

[NPS-PM-04-017](#) Matthews, David. The New Joint Capabilities Integration Development System (JCIDS) and Its Potential Impacts upon Defense Program Managers. December 2004.

[NPS-LM-04-014](#) [Apte](#), Aruna. Optimizing Phalanx Weapon System Lifecycle Support. October 2004.

[NPS-AM-04-013](#) Franck, [Raymond \(Chip\)](#). Business Case Analysis and Contractor vs. Organic Support: A First-Principles View. September 2004.

[NPS-LM-04-006](#) [Ken Doerr](#), Ken, Donald R. Eaton, and [Ira Lewis](#). Measurement Issues in Performance Based Logistics. June 2004.

[NPS-CM-04-004](#) MBA Team. Update of the Navy Contract Writing, Phase II. June 2004.

[NPS-CM-04-002](#) MBA Team. Marine Corps Contingency Contracting MCI. [Revised Manual](#). December 2003.

[NPS-CM-04-001](#) MBA Team. Update of the Navy Contract Writing, Phase I. December 2003.

[NPS-CM-03-006](#) [Tudor, Ron B.](#) Auto-Redact Toolset for Department of Defense Contracts. September 2003.

[NPS-AM-03-004](#) [Boudreau](#), Michael W., and [Brad R. Naegle](#). Reduction of Total Ownership Cost. September 2003.

[NPS-AM-03-003](#) [Dillard](#), John T. Centralized Control of Defense Acquisition Programs: A Comparative Review of the Framework from 1987-2003. September 2003.

[NPS-CM-03-001](#) MBA Team. Transformation in DoD Contract Closeout. June 2003.

Working Paper Series

[NPS-PM-06-002](#) Dillard, John T. When Should You Terminate Your Own Program? November 2005.

[NPS-AM-06-001](#) Naegle, Brad. Developing Software Requirements Supporting Open Architecture Performance Goals in Critical DoD System-of-Systems. November 2005.

[NPS-AM-05-010](#) Zolin, Roxanne V., and [John T. Dillard](#). From Market to Clan: How Organizational Control Affects Trust in Defense Acquisition. June 2005.

[NPS-AM-05-005](#) [Boudreau](#), Michael. Cost as an Independent Variable (CAIV): Front-End Approaches to Achieve Reduction in Total Ownership Cost. June 2005.

[NPS-AM-05-002](#) Yoder, [Elliott Cory](#). The Yoder Three-Tier Model for Optimizing Contingency Contracting Planning and Execution. December 2004.

[NPS-AM-05-001](#) Yoder, [Elliott Cory](#). Engagement versus Disengagement: How Structural & Commercially-Based Regulatory Changes have Increased Government Risks in Federal Acquisitions. November 2004.

[NPS-CM-04-016](#) Stevens, Brett. An Analysis of Industry's Perspective on the Recent Changes to Circular A-76. October 2004.

[NPS-CM-04-012](#) Rairigh, Beth. Air Force Commodity Councils: Leveraging the Power of Procurement. September 2004.

[NPS-CM-04-011](#) [Engelbeck](#), R. Marshall. Using Metrics to Manage Contractor Performance. September 2004.

[NPS-LM-04-009](#) Eaton, Donald R. Improving the Management of Reliability. August 2004.

[NPS-AM-04-007](#) [Naegle](#), Brad R. The Impact of Software Support on System Total Ownership Cost. July 2004.

[NPS-LM-04-003](#) Eaton, Donald R. Enablers to Ensure a Successful Force Centric Logistics Enterprise. April 2004.

[NPS-CM-03-002](#) Parker, Christopher and Michael Busansky. Transformation in DoD Contract Closeout. June 2003.

Acquisition Symposium Proceedings

[NPS-AM-05-004](#) Acquisition Research: The Foundation for Innovation. May 2005.

[NPS-AM-04-005](#) Charting a Course for Change: Acquisition Theory and Practice for a Transforming Defense. May 2004.

Technical Reports

[NPS-GSBPP-03-003](#) [Dillard](#), John T. Centralized Control of Defense Acquisition Programs: A Comparative Review of the Framework from 1987-2003. September 2003.

[NPS-GSBPP-03-004](#) [Boudreau](#), Michael W., and [Brad R. Naegle](#). Reduction of Total Ownership Cost. September 2003.

Presentations, Publications and External Forums

Rendon, Rene. "Commodity Sourcing Strategies: Supply Management in Action." Published as "Commodity Sourcing Strategies: Processes, Best Practices, and Defense Initiatives." *Journal of Contract Management* 3, no.1 (2005): 7-21.

Doerr, Ken, Ira Lewis, and Donald Eaton. "Measurement issues in Performance Based Logistics." *Journal of Public Procurement* 5, no. 2 (2005): 164-186.

Eaton, Donald, Ken Doerr, and Ira Lewis. "Performance Based Logistics: A Warfighting Focus." *US Naval Institute Proceedings*. (In Press).

Doerr, Ken, Donal Eaton, and Ira Lewis. "Performance Based Logistics." Presented to the International Defense Acquisition Resource Management Conference. Capellen, Luxembourg, 2004.

Kang, Keebom, and Ken Doerr. Workshop: Metrics and Performance Evaluation in Performance Based Logistics. Presented at Future Naval Plans & Requirements Conference. San Diego, CA. October 2005.

Boudreau, Michael, and Brad Naegle. "[Total Ownership Cost Considerations in Key Performance Parameters and Beyond.](#)" *Defense Acquisition Research Journal* 38, no.2 (2005): 108-121.

Boudreau, Michael, and Brad Naegle. Workshop: Setting up Acquisition for Total Lifecycle Supportability Performance. Presented at the Institute for Defense and Government Advancement Conference: Total Lifecycle Systems Management. Arlington, VA. 2005.

Kang, Keebom, Ken Doerr, Uday Apte, and Michael Boudreau. "Decision Support Models for Valuing Improvements in Component Reliability and Maintenance." Submitted to the *Journal of Defense Modeling and Simulation* in July 2005 for possible publication. Currently the article is being reviewed by referees.

Franck, Raymond (Chip). "Business Case Analysis and Contractor vs. Organic Support: A First-Principles View." Presented at the Western Economic Association International Annual Conference. San Francisco, CA. 5 July 2005.

Dillard, John, and Mark Nissen. "Computational Modeling of Project Organizations under Stress." In review.

Dillard, John. "Centralization of Defense Acquisition Programs." Accepted for publication in the *Defense Acquisition Research Journal* (2005).

Nissen, Mark E., and John Dillard. "Computational Design of Public Organizations." In review.

IS4710 - Qualitative Methods. This research-seminar course has integrated the results of the FY05 Dillard-Nissen research into the students' course project.

[Dillard, John T.](#) "Centralized Control of Defense Acquisition Programs." [IAMOT 2004](#) - New Directions in Technology Management: Changing Collaboration between Government, Industry and University. 3 -7 [April 2004](#).

[Dillard, John T.](#) "Centralized Control of Defense Acquisition Programs: A Comparative Review of the Framework from 1987-2003." BPP Research Colloquium. [25 November 2003](#).

Copies of the Acquisition Sponsored Research Reports may be printed from our website www.nps.navy.mil/gsbpp/acqn/publications

Initial Distribution List

1. Defense Technical Information Center 2
8725 John J. Kingman Rd., STE 0944; Ft. Belvoir, VA 22060-6218
2. Dudley Knox Library, Code 013 1
Naval Postgraduate School, Monterey, CA 93943-5100
3. Research Office, Code 09 1
Naval Postgraduate School, Monterey, CA 93943-5138
4. Robert N. Beck 1
Dean, GSBPP
555 Dyer Road, Naval Postgraduate School, Monterey, CA 93943-5000
5. Keith F. Snider 1
Associate Professor, GB/Sk
555 Dyer Road, Naval Postgraduate School, Monterey, CA 93943-5000
6. James B. Greene 1
Acquisition Chair, GB/Jg
555 Dyer Road, Naval Postgraduate School, Monterey, CA 93943-5000
7. Bill Gates 1
Associate Dean for Research, GB/Gt
555 Dyer Road, Naval Postgraduate School, Monterey, CA 93943-5000
8. Aruna Apte 1
Assistant Professor, GB
555 Dyer Road, Naval Postgraduate School, Monterey, CA 93943-5000
9. Eugene Dutkowski 1
Naval Surface Warfare Center, Crane, Indiana
10. Karey L. Shaffer 1
Program Manager, Acquisition Research Program, GB/Ks
555 Dyer Road, Naval Postgraduate School, Monterey, CA 93943-5000

Copies of the Acquisition Sponsored Research Reports may be printed from our website www.nps.navy.mil/gsbpp/acqn/publications
